

DISCLAIMER


Electronic versions of the exhibits in these minutes may not be complete.

This information is supplied as an informational service only and should not be relied upon as an official record.

Original exhibits are on file at the Legislative Counsel Bureau Research Library in Carson City.

Contact the Library at (775) 684-6827 or library@lcb.state.nv.us.

MEDICAID MANAGEMENT INFORMATION SYSTEM (MMIS)

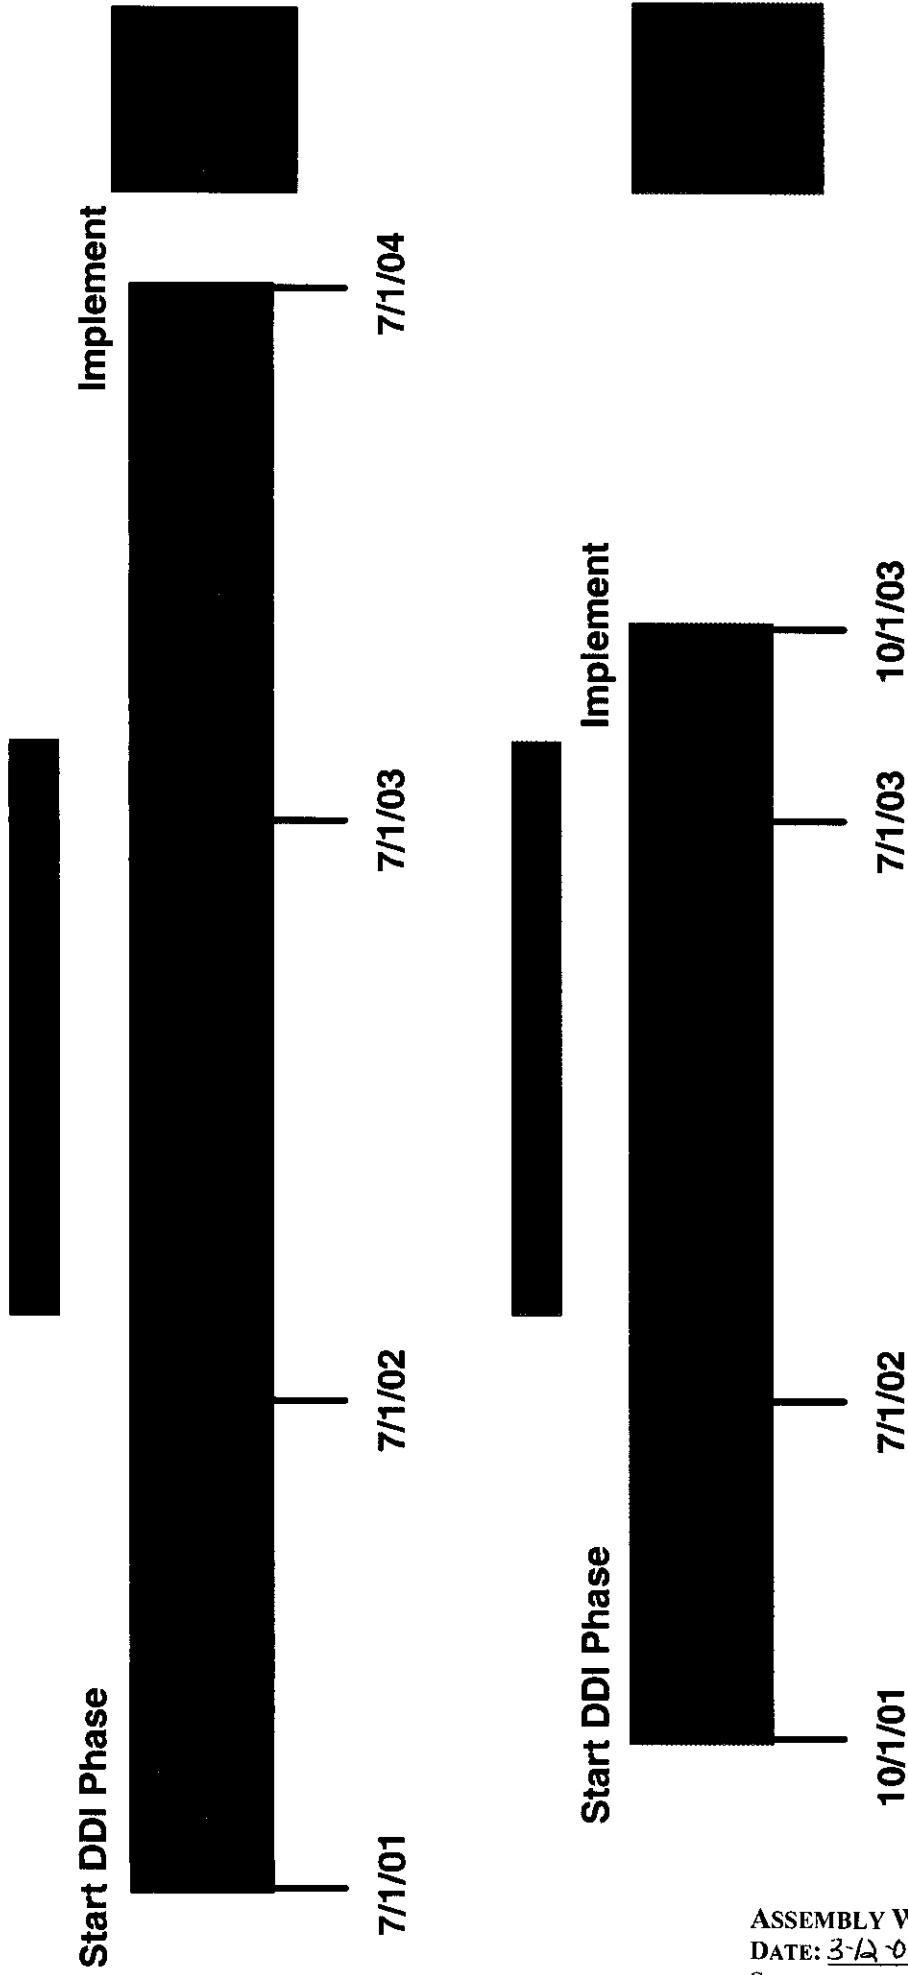

Cost Savings	
DDI	\$ 3.7M
HIPAA Retro	<u>\$10.0M</u>
	\$13.7M

J 1084

Pharmacy POS		Original	Revised
Task Name	Start Date	Finish Date	Finish Date
Nevada First SX Implementation	Thu 9/5/02	Mon 2/17/03	Mon 2/17/03
Design and Construction Phase	Mon 12/9/02	Thu 1/23/03	Thu 1/23/03
Submit Capacity Analysis Document to NV	Fri 12/13/02	Fri 12/13/02	Fri 12/13/02
Submit DSD to NV	Mon 12/16/02	Mon 12/16/02	Mon 12/16/02
Submit System Documentation to NV	Thu 1/23/03	Thu 1/23/03	Thu 1/23/03
Training Phase	Mon 9/16/02	Tue 2/4/03	Tue 2/4/03
Cultural Change Management	Fri 11/29/02	Tue 2/4/03	Tue 2/4/03
Deliver Cultural Change Management Plan (Deliv. #15)	Thu 1/23/03	Thu 1/23/03	Fri 4/18/03
Help Desk	Mon 12/16/02	Thu 1/23/03	Thu 1/23/03
"Deliver Help Desk Procedures, Protocol, Staffing and Training Plan (Deliv. #17)"	Thu 1/23/03	Thu 1/23/03	Thu 1/23/03
Online User Procedure and User Documentaton to NV	Thu 1/23/03	Thu 1/23/03	Thu 1/23/03
Implementation Phase	Mon 1/20/03	Fri 1/31/03	Fri 1/31/03
Move to production environment	Fri 1/24/03	Fri 1/31/03	Fri 1/31/03
Implement the NV POS	Fri 1/24/03	Fri 1/31/03	Fri 1/31/03
Implementation of Interfaces Document to NV	Fri 1/24/03	Fri 1/24/03	Fri 1/24/03
Pilot Operations Document to NV	Fri 1/24/03	Fri 1/24/03	Fri 1/24/03
GO LIVE		Sat 2/1/03	Sat 2/1/03

Full Medicaid Management Information System (MMIS)		Original	Revised
Task Name	Start Date	Finish Date	Finish Date
Planning and Administration Phase	Mon 9/23/02	Fri 6/11/04	Fri 6/11/04
Requirements Validation and Demonstration Phase	Tue 10/8/02	Thu 3/27/03	Thu 3/27/03
System Modifications	Fri 10/4/02	Mon 4/14/03	Mon 4/14/03
Configuration Management	Mon 11/25/02	Wed 1/22/03	Fri 3/7/03
"Design, Development and Implementation of Interfaces including HIPAA"	Mon 11/25/02	Prior to Wed 10/1/03	Prior to Wed 10/1/03
System Enhancements/Modifications	Wed 10/9/02	Fri 8/29/03	Fri 8/29/03
Testing (System/Integration)	Mon 12/2/02	Fri 8/29/03	Fri 8/29/03
Data Conversion	Mon 9/16/02	Thu 9/18/03	Thu 9/18/03
Pilot Operations	Tue 7/15/03	Fri 9/12/03	Fri 9/12/03
Training	Mon 9/16/02	Tue 9/16/03	Tue 9/16/03
Cultural Change Management Plan	Fri 11/1/02	Fri 4/18/03	Fri 4/18/03
Cultural Change Management Help Desk	Fri 11/1/02	Thu 10/2/03	Thu 10/2/03
User and Systems Documentation	Mon 6/2/03	Fri 7/25/03	Fri 7/25/03
Business Resumption Plan	Tue 10/8/02	Mon 7/14/03	Mon 7/14/03
Fully Operational MMIS	Thu 1/2/03	Wed 9/24/03	Wed 9/24/03
		Wed 10/01/03	Wed 10/01/03

Decision Support System (DSS)		Original	Revised
Task Name	Start Date	Finish Date	Finish Date
NV DSS Implementation	Tue 8/13/02	Tue 10/14/03	Tue 10/14/03
Project Planning	Tue 8/13/02	Fri 11/8/02	Fri 11/8/02
Project Management	Thu 10/10/02	Tue 10/14/03	Tue 10/14/03
Requirements Validation and Demonstration	Mon 9/30/02	Wed 12/18/02	Mon 3/31/03
Implement Technical Environment	Mon 11/11/02	Mon 3/10/03	Mon 3/10/03
Perform Data Extraction/Verification	Fri 10/25/02	Fri 4/4/03	Fri 4/4/03
System Modification	Fri 10/25/02	Wed 3/5/03	Fri 3/7/03
Configuration Management	Mon 11/11/02	Fri 12/27/02	Mon 3/17/03
Development and Implementation of Interfaces	Tue 12/10/02	Wed 4/9/03	Wed 4/9/03
System Testing / Data Conversion	Tue 4/1/03	Wed 8/6/03	Wed 8/6/03
Production Build	Tue 6/17/03	Thu 9/25/03	Thu 9/25/03
Pilot Operations	Fri 6/20/03	Mon 10/13/03	Mon 10/13/03
Training	Wed 3/5/03	Thu 10/9/03	Thu 10/9/03
Transition Planning	Fri 9/5/03	Fri 9/12/03	Fri 9/12/03
Cultural Change Management Plan	Fri 11/1/02	Fri 4/18/03	Fri 4/18/03
Cultural Change Management	Wed 7/2/03	Tue 9/23/03	Tue 10/14/03
Help Desk	Wed 7/16/03	Wed 9/10/03	Wed 9/10/03
User and Systems Documentation	Tue 7/22/03	Fri 9/19/03	Fri 9/19/03
Business Resumption Plan	Fri 8/8/03	Thu 10/9/03	Thu 10/9/03
Fully Operational System – DSS (Deliv. #23)		Mon 10/13/03	Mon 10/13/03
